




CONSIGLI

Est. 1905

WINCHESTER HIGH SCHOOL – SCHEDULED WORK UPDATE

Week of 6/11/2017

- Building A:
 - Installation of the stair A curtain wall glass completed. Trim install to begin next week.
 - Marker board & tack board installation is complete on the first floor.
 - Leveling is ongoing on first floor corridors, VCT install ongoing on second floor.
 - Wood door installation is complete on all floors.
 - HM door installation ongoing in Stair A.
 - Final painting is complete on the second floor, and painting started in Stair A.
 - Fin tube radiator covers are being installed on first floor.
 - Ceilings are being flooded on the first and second floors.
- Building B:
 - Washing and waxing floor ongoing on all three floors.
 - Corridor tile returns at the main corridors on all floors is ongoing.
- Site work:
 - Stair A structural slab and walkway installation is ongoing.
 - Spreading top soil at Skillings field.
 - Prepping and subgrading for concrete plaza south of Bldg A.
 - Plantings completed at Skillings Field.
- Weekend Work (Saturday 6/10/17):
 - VCT install & waxing floors in building A.

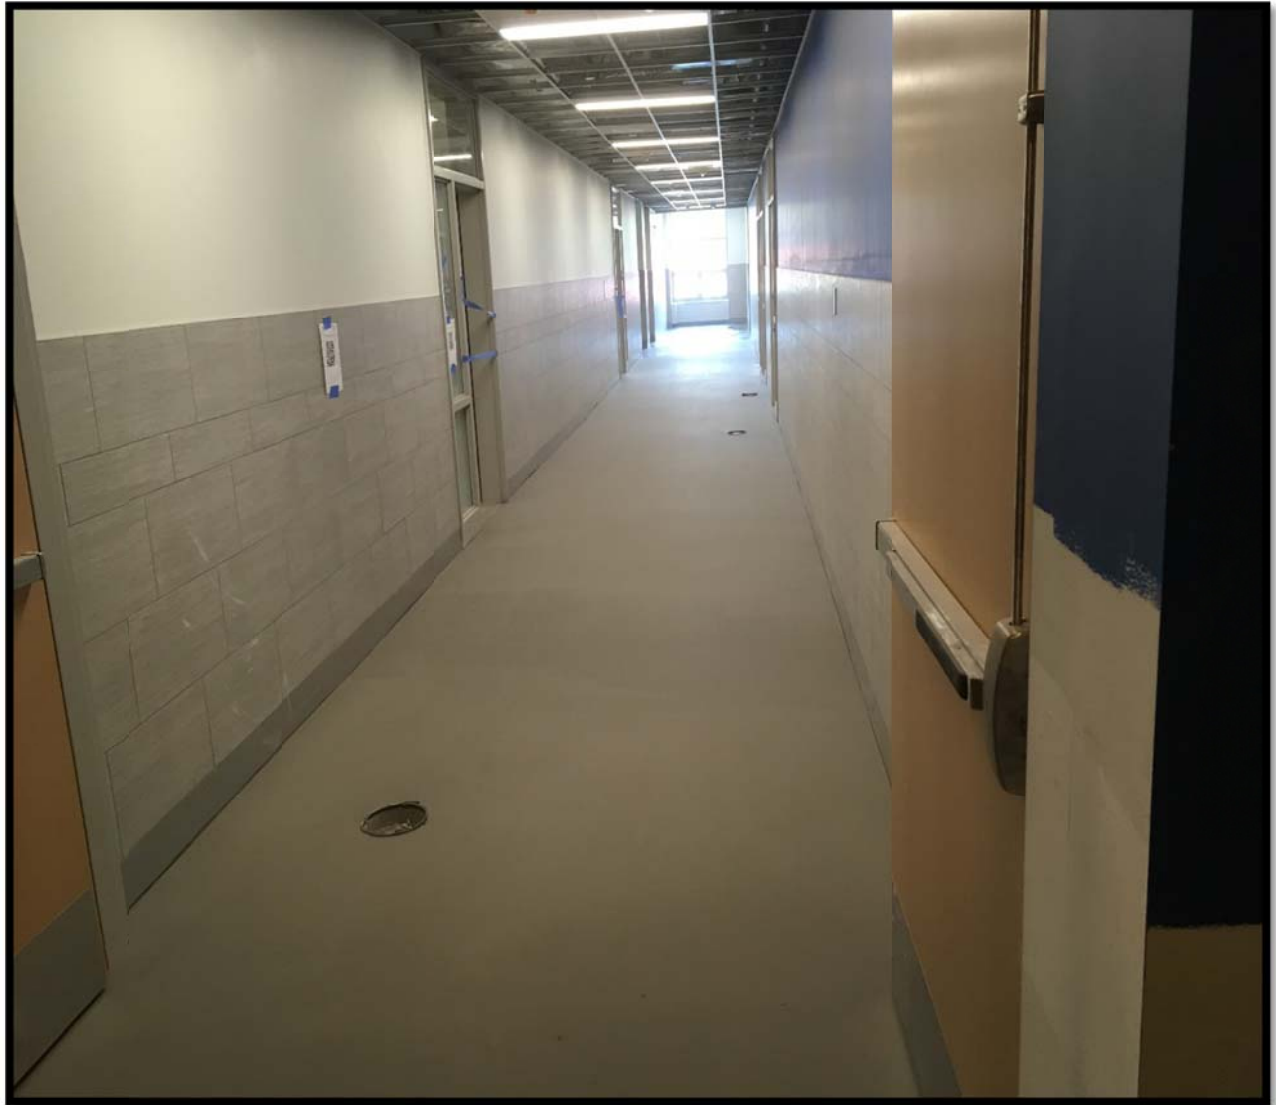

Bldg A Lvl 1: Leveling & Installing VCT in Corridors



Bldg A South: Prepping/Subgrading for Concrete Plaza



Bldg A East: Pouring Concrete Walkways to Entrances



Skillings Field: Installing Trees, Bollards, & Top Soil
